

NORTHERN PACIFIC RAILWAY CO.
AUTHORITY FOR EXPENDITURE

COMPTROLLER'S RECORD
1923
Year: 1923

Superintendent's No. **7** Dept. No. Engineering Dept. No. **23(23)** A. F. E. NO. **107**
Tacoma Div. American Lake District State Wash Val. Sec. No. **27-A**
Line Branch

AUTHORITY IS REQUESTED FOR A NET EXPENDITURE OF \$ 340.

Accounting distribution as follows: (Distribution to be made in General Office.)

	Operating Expenses	Profit and Loss	Net Operating Expenses	Net Profit and Loss
Cost of property retired	\$	\$	\$	\$
Value of salvage				
Incidental costs				
Total to Operating Expenses				
Total to Profit and Loss				
To Material and Supplies				
To Bills for Collection				
To Other Accounts				
Net charge to investment account—Additions and Betterments				340
Total of distribution				\$ 340



Budget reference: *not in Budget* Class of Work: No. *31*
Joint facility contract reference: **OWRR&N Co 12-29-17** Addition
Month: **SEP** 1923

The location is on this company's property. To secure rights, it will be necessary

Location: **American Lake, Washington**

Title **Placing inside guard rail on sharp curve on Black Powder Spur and**

Reason: **Track serving black powder plant of E. I. du Pont de Nemours & Co at American Lake is on a sharp curve and on trestle, this trestle constructed and maintained by Messrs. du Pont de Nemours & Company, track metal furnished under contract by Northern Pacific. There have been several derailments on this curve. September 11, 1922 tank of engine 213 derailed and came very near going over the side of the trestle, necessary to use wrecking outfit from Tacoma to rerail this engine tank. To safeguard against further derailments, inside guard rail has been installed and this estimate submitted to cover completed work and adjusting property account, all as per sketch and estimate herewith attached.**

Work completed December, 1922.

~~Work completed~~ company force under charge of Superintendent

Accounting to concentrate in the office of Superintendent

Signature and Title: *[Signature]* Superintendent Date **Jan. 8,** 19 **23**

APPROVED:


[Signature] General Superintendent. *[Signature]* Prin. Asst. Engr. or Engr. in Charge. *[Signature]* Assistant General Manager.

[Signature] Mech. Supt., Supt. Trough, or Signal Engr. *[Signature]* Chief Engineer. *[Signature]* General Manager. *[Signature]* Vicg. President.

[Signature] For Comptroller. *[Signature]* President. Date of Final Approval } **7 26 23** 19

COMPTROLLER'S RECORD OF NOTICE OF APPROVAL AND OF COMPLETION

Form No. 1345 issued **JAN 31 1923** Work begun 19 Work finished **Oct. 29, 1922**

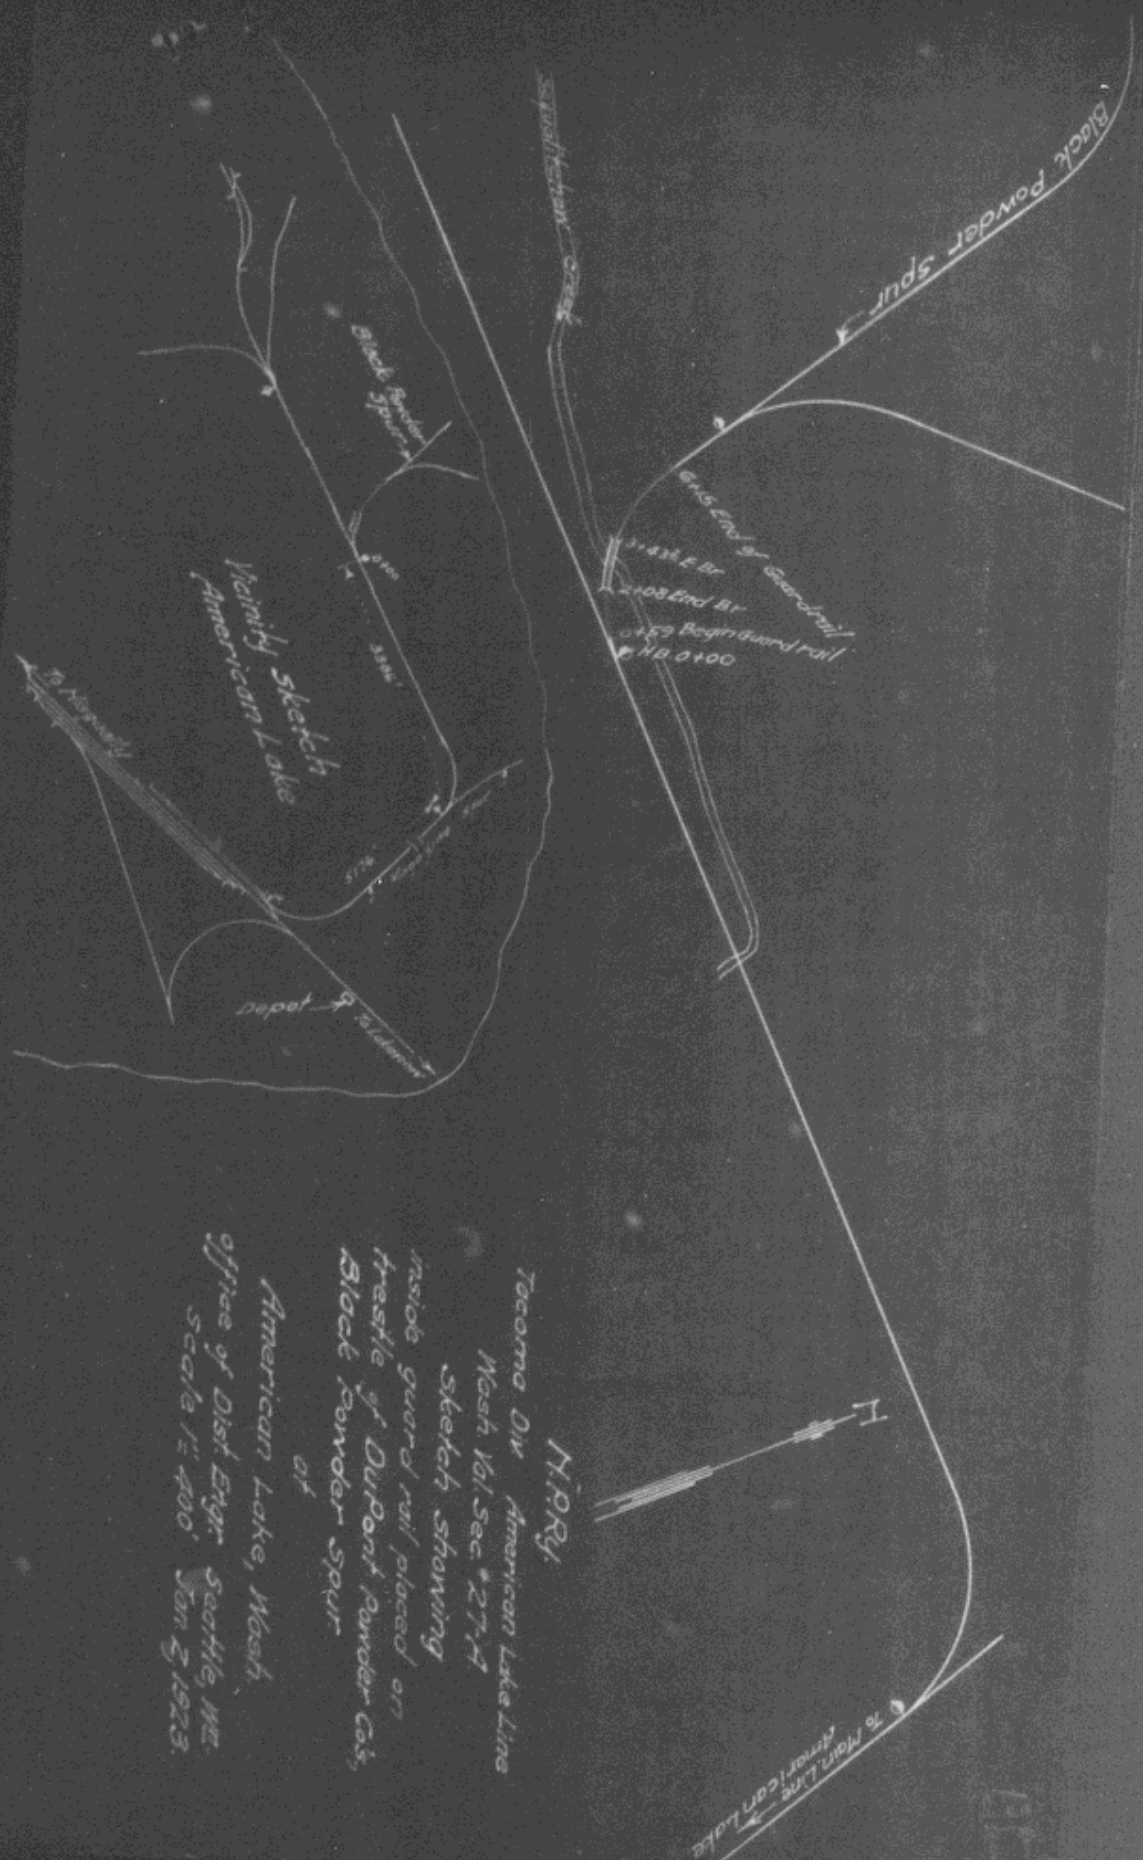

N.P.Ry.
 Tacoma Div American Lake Line
 Wash Val. Sec. # 2714
 sketch showing
 inside guard rail placed on
 trestle of DuPont Powder Co's
 Black Powder spur
 of
 American Lake, Wash.
 office of Dist. Engr. Seattle, Wn.
 scale 1" = 400' Jan 2, 1923.
